### Renaissance Reclaimed, LLC

13 Walnut St.

Decatur, AL 35601 US

(864) 844-1753

sw@renaissancereclaimed.com

www.renaissancereclaimed.com



### **INVOICE**

BILL TO

Wolfe Homes

200 Pomona Dr. Suite J

Greensboro, North Carolina

27407-1637 United States

INVOICE

1186

DATE

08/25/2023

TERMS

Due on receipt

DUE DATE

08/25/2023

DATE	ACTIVITY	DESCRIPTION	QTY	RATE	AMOUNT
07/14/2023	Service - SG	worked on kitchen arch window boxes facing the lake.	11.50	125.00	1,437.50
07/19/2023	Service - SG	worked on cutting templates for master bedroom window, helped on dinning room header, got double doors to the 2nd floor facing the street.	6.50	125.00	812.50
07/22/2023	Service - SG	Worked on master bedroom windows, cleaned up, door casings on 2nd floor sanding, edges, sanding on base that meets door casings, glue up and pin nailed arch casings had a spit in the top, promed steel beam cut pressure treated lumber primed it as well.	7.50	125.00	937.50
07/30/2023	Service - CC	came home	8	55.00	440.00
07/30/2023	Service - SG	drove home	8	55.00	440.00
08/03/2023	Service - CC	Drove to Greensboro	8	55.00	440.00
08/03/2023	Service - MW	traveled to Greensboro and packed up supplies	11	55.00	605.00
08/04/2023	Service - MW	cut and squared pocket doors, hung are finished, 2nd floor base/door casings	8	125.00	1,000.00

		straightened tools and cleaned up work space.			
08/08/2023	Service - CC	Finished base at butlers pantry Extended cased opening 3" for corner reworked base. Framed out the accordion door/cased/trimmed.	9.50	125.00	1,187.50
08/08/2023	Service - MW	turned the back door around an all hardware that had be turned around on all hinges	9.50	125.00	1,187.50
08/09/2023	Service - CC	Began framing front door fur out, trim window x 3 cleaned up area.	10	125.00	1,250.00
08/10/2023	Service - CC	pocket door rework and reframe.	11	125.00	1,375.00
08/12/2023	Service - CC	Pocket door 2nd floor laundry and clean up	6	125.00	750.00
08/12/2023	Service - MW	Pocket doors, hanging two upstairs and trimmed them out and cleaned up.	4	125.00	500.00
	Service - CC	Driving to NC	8	55.00	440.00
	Service - CC	Ran base downstairs cased opening framed for pockets helped stephen with window removal	8.50	125.00	1,062.50
	Service - CC	Cut casing for upstairs began install run some base downstairs base incomplete	9	125.00	1,125.00
	Service - CC	Casing doors 2nd floor incomplete	8	125.00	1,000.00
	Service - CC	Fixed window stool and trimmed doors 3rd floor	10	125.00	1,250.00
	Service - CC	flush cut shims off door jambs, removed front door upacked front door cased doors 2nd floor	10.50	125.00	1,312.50
	Service - CC	trimmed doors on 2nd floor cut started	10	125.00	1,250.00

Service - CC	Door jams and baseboards 2nd floor	11	125.00	1,375.00
Service - CC	base boards doors 2nd floor steam sander	12.50	125.00	1,562.50
Service - CC	base 2nd floor steam sander	9	125.00	1,125.00
Service - CC	base 2nd floor	4	125.00	500.00
Service - CC	base 2nd floor steam	10	125.00	1,250.00
Service - CC	door casings 2nd floor remove exterior garage cased out made threshold	10	125.00	1,250.00
Service - CC	threshold back garage door glue down base in that area cased out by stairwell cased out doors 2nd floor some base checked au electrical outlets.	12	125.00	1,500.00
Service - CC	cased doors 1st floor	5	125.00	625.00
Service - CC	clean up	5	125.00	625.00
Service - MW	framed in closet 3rd floor, bath closed in some doors addes some studs were needed on straightenin gsome walls	10	125.00	1,250.00
Service - MW	tore out doors and windows on first floor one in front and 3 on back	10.50	125.00	1,312.50
Service - MW	put frame off front door and header in moved some door around	10	125.00	1,250.00
Service - MW	done windows up 3rd floor finished head on 1st floor 2 arches 3rd floor	11	125.00	1,375.00
Service - MW	fured bathroom 2nd put hangers on 3rd finished up 3rd floor	10.50	125.00	1,312.50
Service - MW	blocked hangers 3rd floor finished fur bathroom tore out another bath on 2nd floor	9	125.00	1,125.00
Service - MW	fixed two windows 3rd floor and started on 3rd	10	125.00	1,250.00

Service - MW	finished window on 3rd	10	125.00	1,250.00
Service - MW	finished front door and furred bathroom 2nd floor	9.50	125.00	1,187.50
Service - MW	Built two arches	9	125.00	1,125.00
Service - MW	Windows and 3 doors	9	125.00	1,125.00
Service - MW	Cleaned up	5	125.00	625.00
Service - SG	Left for NC	17	55.00	935.00
Service - SG	Unloaded truck and set up work area. Helped floor crew with cutting floor ends square	10	125.00	1,250.00
Service - SG	cut back sheetrock pulled nails and screws for baseboard cut back corners on doorways	11	125.00	1,375.00
Service - SG	continued cutting out sheetrock corners in doorways. Cut plywood pocket jigged plywood for wall in kitchen. Helped with staircase templates.	11	125.00	1,375.00
Service - SG	clean up organize work area, finish putting up the wall in the kitchen area.	3.50	125.00	437.50
Service - SG	took measurements of entire house, drawings of each room windows- doorways. started tearing out windows getting ready for casings.	12	125.00	1,500.00
Service - SG	tore out windows in living room and building casings.	9.75	125.00	1,218.75
Service - SG	got main room cleaned out trim moved to kitchen to make room for the lift, cutting plywood to build living room kitchen area window boxes.	10	125.00	1,250.00
Service - SG	worked on window casings helped with door casings and templates for the back door glue up and nail	10	125.00	1,250.00

	belt sanded arches for back door.			
Service - SG	continued working on arch windows in kitchen cutting pcs assembly prep work bondo sanding ect.	8.50	125.00	1,062.50
Service - SG	worked on redoing arch window pcs. assembly	10	125.00	1,250.00
Service - SG	worked on assembled boxes for arch windows set/screwed in place bondo sand broke edges caulked in clean to the windows ready for primer. Got living room windows out stacked on back porch	10.50	125.00	1,312.50
Service - SG	Got double door up to 3rd floor after meeting. Started guys on the back porch and garage area cleaning and organizing. Started back on templates for arch windows in the master bedroom measuring cutting 1/4th inch and transferring to 3/4 inch plywood.	8	125.00	1,000.00
Service - SG	Got bolts to start the brackets on the 3rd floor ahead of sheet rocker brakets, marked holes, drilled brackets put in place checked level. Helped get triangle glass window out, ply wood in place, screwed in place rough sand and bondo in between worked on master arch windows.	9	125.00	1,125.00
Service - SG	Master bedroom casings had to be trim down to make fit got center pcs cut and glued up dry fitted ready for bottoms archs and tops.	9.50	125.00	1,187.50
Service - SG	Scribing sides to fit marking centers to assemble master	10	125.00	1,250.00

	bedroom windows. Metal beams cleaned primed pressure treated wood to mount to beams, cut to size and primed. Organized and cleaned kitchen area, went back to scribbing master bedroom windows.			
Service - SG	continued scribbing master bedroom windows last two sides and started putting them together. sanded bondo off of window shelves, cutting arch pcs.	9	125.00	1,125.00
Service - SG	Finish up arch window tops to get the casing assembled for master bedroom cut bendable plywood, glue pin nail to arch cuts.	7.50	125.00	937.50
Service - SG	Worked on master bedroom windows, helped install glass in front doors caulked in black and trim attached	10	125.00	1,250.00
Service - SG	Clean up, load trailer will all tools and boxes	5	125.00	625.00
Service - CC	cut and squared pocket doors, hung are finished, 2nd floor base/door casings straightened tools and cleaned up work space.	8	125.00	1,000.00
Service - CC	Pocket door/ Butlers pantry 1st floor door casings, 2nd floor door jambs/adjust and screwed	10	125.00	1,250.00
Service - CC	Exterior door	6	125.00	750.00
Service - CC	Made adjustments to butlers pantry pocket exterior door and window. Moved debris out of living room, run base from MBR to fireplace.	10.50	125.00	1,312.50
Service - CC	Rework/Reframe pocket door MB sorted	10	125.00	1,250.00

	pocket door 2nd floor laundry			
Service - CC	Traveled home	8	55.00	440.00
Service - MW	worked on the led light in upstairs hallway worked on some pocket doors on first floor.	10	125.00	1,250.00
Service - MW	Exterior doors first floor	6	125.00	750.00
Service - MW	worked on back door and window on top redoing jambs for door.	10.50	125.00	1,312.50
Service - MW	jamming the kitchen door and put header in on kitchen window and jambs.	10	125.00	1,250.00
Service - MW	finished jamming out the kitchen doors and windows and cleaned up	11	125.00	1,375.00
Service - MW	started putting in pocket door and hard ware casing on them.	10	125.00	1,250.00
Service - MW	Traveled home	8	55.00	440.00
Service - SW	Total hours working install - 1st trip	260	125.00	32,500.00
Service - SW	Total hours working install - 2nd trip	135	125.00	16,875.00
Service - SW	total hour - 3rd trip	63	185.00	11,655.00
	SUBTOTAL			141,178.75
	TAX			0.00
	TOTAL			141,178.75
	BALANCE DUE			\$141,178.75

### Renaissance Reclaimed, LLC

13 Walnut St.
Decatur, AL 35601 US
(864) 844-1753
sw@renaissancereclaimed.com
www.renaissancereclaimed.com



## **INVOICE**

#### **BILL TO**

Wolfe Homes 200 Pomona Dr. Suite J Greensboro, North Carolina 27407-1637 United States **INVOICE #** 1185 **DATE** 08/25/2023 **DUE DATE** 08/25/2023 **TERMS** Due on receipt

DATE	ACTIVITY	DESCRIPTION	QTY RATE	AMOUNT
07/03/2023		1/4" Birch White plywood		780.00
07/03/2023		1/2" Pro grade maple plywood		871.39
07/03/2023		3/4" Pro grade maple plywood		1,127.49
	Services	Odies oil	4,524.54	4,524.54
	Services	HD tools		5,682.47
	Services	HD		1,864.77
	Services	HD		314.47
	Services	HD		406.36
	Services	HD		189.37
	Services	HD		248.40
	Services	HD		36.02
	Services	Wurth		1,167.96
09/22/2022		Mattern- glass for vanity		637.48
09/22/2022		Processing Fee MasterCard Cross Border fee for LitFAD		5.73
07/03/2023		3/8" 8x4 Bending Lauan (plywood)		1,044.42
07/11/2023		HD invoice number 185880		205.43
07/11/2023		Supplies for Mattern		1,491.00

DATE	ACTIVITY	DESCRIPTION	QTY	RATE	AMOUNT
07/12/2023		epoxy for mattern job			1,722.71
07/13/2023		Ratchet Straps, cutting tools, and saw blades			283.23
07/19/2023		Bending plywood			455.65
07/19/2023		Pro cab maple			1,465.75
07/21/2023		HD Invoice number 27153			197.59
					Subtotal: 24,722.23
	Services	Poplar Doors	31	500.00	15,500.00
	Services	Cherry Doors	8	700.00	5,600.00
	Services	hidden door jamb assembly with standard stops	39	176.77	6,894.03
	Services	hidden door jamb assemblies with push through stops	7	288.84	2,021.88
	Services	1 x 3/8 thermal base finish trim	127	20.64	2,621.28
	Services	1x1 shoe mold	83	36.64	3,041.12
	Services	specialty shadow bead 8" base board	54	78.24	4,224.96
			ГОТАL		64,625.50
		TAX TOTA	<b>4</b> I		0.00 64,625.50
			ANCE DUI	Ξ	<b>\$64,625.50</b>
					Ψυ 190±2000

## Renaissance Reclaimed, LLC

13 Walnut St.
Decatur, AL 35601 US
(864) 844-1753
sw@renaissancereclaimed.com
www.renaissancereclaimed.com



## **INVOICE**

### BILL TO

Wolfe Homes 200 Pomona Dr. Suite J Greensboro, North Carolina 27407-1637 United States

\$8,719.13

DATE	ACTIVITY	DESCRIPTION	QTY	RATE	AMOUNT	
	Services	Per diems and fuel charges acquired	1	8,719.13	8,719.13	

BALANCE DUE

#### Hannah Tatum

From:

sergio gomez <gsergio11.sg@gmail.com>

Sent:

Wednesday, September 6, 2023 11:58 AM

To:

Invoices

Subject: Stucco, done

5407 Eastern Shores , the stucco repairs on dormers and replace the caulking, add the repairs on extra details, chimneys , add the balcony walls, everything be done today, please make the check to B&B Construction total \$14k let me know how and when I can get it. Anything call me 336 554 0049, Sergio

Wally Overman Plumbing, Inc.

303 Waverly Way Greensboro, NC 27403

# Invoice

DATE	INVOICE#
9/5/2023	12171

BILL TO

Wolfe Homes
200 J. Pomona Dr.
Greensboro, NC 27407

TERMS	Project
Due on receipt	Eastern Shores - Ma

DESCRIPTION	QTY	RATE	AMOUNT
Roughed in tub faucet for the master bathroom. Also roughed in for a personal shower on the third floor and made a repair to a tub spout.			
Labor and Material NC Sales Tax		1,500.00 6.75%	1,500.00 0.00
Thank you for your business!		Total	\$1,500.00

#### **AVE Integration**

811 E Mountain St Kernersville, NC 27284 +1 3365432930 accounting@aveintegration.com



#### INVOICE

BILL TO Wolfe Homes 200 Pomona Dr, Ste J Greensboro, North Carolina 27407 United States

Please be advised that we will charge 1.5% interest per month on late invoices.

SHIP TO Wolfe Homes 200 Pomona Dr, Ste J Greensboro, North Carolina 27407 United States 

 INVOICE
 2021587

 DATE
 09/10/2023

 TERMS
 Net 15

 DUE DATE
 09/25/2023

JOB

EL-5407 E. Shores

DATE	DESCRIPTION		AMOUNT
09/01/2023	Makeup connection in boxes for outle	ets and find wire in Sheetrock for ceiling lights	306.00
09/01/2023	Makeup connection in boxes for outle	ets and find wire in Sheetrock for ceiling lights	204.00
09/01/2023	Makeup connection in boxes for outle	ets and find wire in Sheetrock for ceiling lights	65.00
09/01/2023	Makeup connection in boxes for outle	ets and find wire in Sheetrock for ceiling lights	65.00
09/01/2023	Installed 10 cut in boxes in baseboar	rd removed old boxes	378.00
09/01/2023	Added outlet boxes in baseboards		234.00
09/01/2023	Materials		71.69
09/04/2023	Materials		64.81
09/06/2023	Put a temporary dimmer switch on kit	tchen trims and put 27k 30k and35k color temperature	119.00
09/06/2023	Put a temporary dimmer switch on kit	tchen trims and put 27 30 and 35k color temperature.	91.00
09/08/2023	Pulling low voltage wire for garage d	oors and adding 2 outlets for garage door motors	555.33
09/08/2023	Pulling Iv wire for garage doors and	adding 2 outlets for garage motor.	424.67
09/09/2023	Pulling cat-6 to 2 garage motors pull more outlets for those 2 motors	ling 18-2 wire to the other 2 garage in gym and add 2	484.50
09/09/2023	Pulling cat-6 to 2 garage motors pull more outlets for those 2 motors	ling 18-2 wire to the other 2 garage in gym and add 2	255.00
09/09/2023	Pulling cat 6 to 2 garage motors. pull more outlets for those 2 motors.	ling 18/2 wire to the other 2 garage in gym and add 2	370.50
09/09/2023	Pulling cat 6 to 2 garage motors. pull more outlets for those 2 motors.	ling 18/2 wire to the other 2 garage in gym and add 2	195.00
Thank you for your business and yo much!	our prompt payment. We appreciate it very	SUBTOTAL	3,883.50
		TAX	0.00

TOTAL

3,883.50

BALANCE DUE

\$3,883.50



Triad Door Service

## Galloni's Triad Door Service, Inc

Wolfe Homes 200 J Pomona Drive Greensboro, NC 27407

invoices@wolfehomes.com

\$734.97
Upon receipt
Sep 07, 2023
#30834

SERVICE ADDRESS

5407 Eastern Shores Dr Greensboro, NC 27455

CONTACT US

101 Depot St Jamestown, NC 27282

(336) 887-1612

mbkepley@gmail.com

Service completed by: Jeremy Teer, Phil Spahr

#### INVOICE

Services	qty	unit price	amount
Residential Service	4.0	\$170.00	\$680.00
9/7/23 Take down all 4 doors incl all track, motors, wires, and backhangs.			

Discussed wiring requirements with Stephen as well as mounting details and operator options.

Hauled off and disposed of materials in recycling dumpster.

Note: Any unsatisfactory work must be reported to this office within ten days or job will be considered acceptable.

Materials	qty	unit price	amount
Fuel	1.0	\$8.50	\$8.50

Total	\$734.97
Sales Tax (6.75%)	\$46.47
Total Tax	\$46.47
Subtotal	\$688.50

It's Our Pleasure to Serve You!

0.000

Statement DATE - 10 23 ECEIVE	
TO WOCFE HOMES SEP 11 2023	
BY:	
ATTN. THY WOR SMITH	
IN ACCOUNT WITH	
FROM: CHAMICS PRICE	
	Į
5407 RASTAUN SHORES	-
C/1/2/1/6/1/2	-
CHUCK 40HB	-
1750N 38HR \$2730.00	2
1011 2014	
101AL \$ 2730 Q	2
	_
14W 9-5-23	
7/1/00 1-3-23	
CURRENT OVER 30 DAYS OVER 60 DAYS TOTAL AMOUNT TOTAL AMOU	2
28 Brians, DC2812	01-11

## INVOICE

DATE

INVOICE #

CUST#

9/19/2023

0000007982

0000718

BILL TO:

Wolfe Construction 200 J Pomona Drive Greensboro NC 27407

Wade's Heating & A/C

Wade's Oil Company Inc. PO BOX 88

Mcleansville NC 27301 Phone: 336-697-0300

SHIP TO:

Wolfe Construction 200 J Pomona Drive Greensboro NC 27407

P.O. NUMBER	100	TERMS	SALES PEI	NAME OF TAXABLE PARTY.
MATTERN JOB		UPON RECEIPT	THOMAS P	-
QUAN		DESCRIPTION	PRICE EACH	AMOUNT
1.00	System for Permit # 2 Set Air Har Tie in Duc Check Gar Fireplaces Finish Duc side of ho	ctwork for 2nd and 3rd floors for System on Left buse Gas Piping to 3rd Floor Fireplace outside of	7,500.00	7,500.00
	TOTAL			\$7,500.00

3567 Jess Smith Road Sophia, NC 27350 Phone: (336) 434-7433 Fax: (336) 434-1052 Email: ChampionTileCo@aol.com



Invoice Date: **09/22/2023**Invoice Number: **005982** 

Page 1 of 1

Ceramics • Marble • Pavers

#### INVOICE

Name WOLFE HOMES

Address 220-J POMONA DRIVE

City, ST Zip GREENSBORO, NC 27407

james.wolfe@wolfehomes.com

Phone (336) 268-2018

Cell (336) 314-5146

Fax (336) 299-2949

Job Desc. 5407 EASTERN SHORES / BANDING

Qty.	Units	Description	Price	Amount
1031.00		BANDING LABOR ONLY. BANDING WHERE TILE DOE NOT GET INSTALLED. MASTER BATH AND UP GUEST BATH	3.00	3093.00
16.00	EACH	BANDING MATERIALS	75.00	1200.00

We look forward to working with you again!

**Total:** \$4,293.00



3567 Jess Smith Road Sophia, NC 27350 Phone: (336) 434-7433 Fax: (336) 434-1052

Email: ChampionTileCo@aol.com



Proposal Date: **08/18/2023** 

Proposal Number: 005977

Page 1 of 4

### Ceramics • Marble • Pavers

## PROPOSAL

Name WOLFE HOMES

Address 220-J POMONA DRIVE

City, ST Zip GREENSBORO, NC 27407

james.wolfe@wolfehomes.com

Phone (336) 268-2018

Cell (336) 314-5146

Fax (336) 299-2949

Job Desc. 5407 EASTERN SHORES GREENSBORO / ANGELA

Qty.	Units	Description	Price	Amount
72.00	SQFT	ANDREWS BATHROOM , TWO TUB WALLS TO CEILING 24 X 48 VERTICAL STACK INSTALLATION * LARGE FORMAT	22.00	1584.00
1.00	EACH	ANDREWS BATHROOM ,WINDOW WALL 80 SQFT MOSAIC TILE INSTALLATION	2800.00	2800.00
27.00	SQFT	ANDREWS BATHROOM , WAINSCOTTING TWO WALLS	20.00	540.00
36.00	SQFT	ANDREWS FLOOR TILE INSTALLATION	20.00	720.00
1.00	EACH	ANDREWS, PREP FLOOR	250.00	250.00
	EACH	*		
1.00	EACH	GUEST BATHROOM WALLS TO 10 FT CEILING. TILE INSTALLATION ON NICHE WALL. ANGELA TO LAY OUT VEINING DIRECTION. 24 X 48 MARBLE.	2800.00	2800.00
1.00	EACH	GUEST BATH, BANDING WALL TILED AREA	325.00	325.00
1.00	EACH	INSTALLATION OF SHOWER FLOOR TILE WITH MITER EDGES 27 SQFT	700.00	700.00
1.00	EACH	GUEST BATH , MUD BED SHOWER FLOOR	825.00	825.00
1.00	EACH	GUEST BATH, WATERPROOFING AND MATERIALS FOR SHOWER TRAY	340.00	340.00
41.00	SQFT	GUEST BATH , FLOOR TILE INSTALLATION	20.00	820.00

Proposal Accepted by

\$42,564.00



Total:

Prices good for 30 days only. We look forward to working for you!

3567 Jess Smith Road Sophia, NC 27350 Phone: (336) 434-7433 Fax: (336) 434-1052

Email: ChampionTileCo@aol.com



Proposal Date: **08/18/2023**Proposal Number: **005977** 

Page 2 of 4

Ceramics • Marble • Pavers

### PROPOSAL

Name WOLFE HOMES

Address 220-J POMONA DRIVE

City, ST Zip GREENSBORO, NC 27407

james.wolfe@wolfehomes.com

Phone (336) 268-2018

Cell (336) 314-5146

Fax (336) 299-2949

Job Desc. 5407 EASTERN SHORES GREENSBORO / ANGELA

Qty.	Units	Description	Price	Amount
1.00	EACH	GUEST BATH PREP FLOOR	325.00	325.00
	EACH	*		
1.00	EACH	MASTER BATHROOM SHOWER FLOOR TILE INSTALLATION WITH MITERED EDGES 36 SQFT	900.00	900.00
1.00	EACH	MASTER BATH, MUD SHOWER FLOOR , LABOR AND MATERIALS	1280.00	1280.00
1.00	EACH	WATERPROOFING MASTER SHOWER FLOOR AND CONTINUED FOR APPROX. FIVE FEET INTO THE MASTER FLOOR AREA FIVE FEET, LABOR AND MATERIALS	540.00	540.00
1.00	EACH	BACK OF NICHE INSTALL DRILL WATER JETS / VALVES , LABOR ONLY, VALVES ARE NOT INCLUDED	490.00	490.00
215.00	SQFT	MASTER BATH FLOOR 12 X 24 MARBLE STACK	20.00	4300.00
1.00	EACH	MASTER PREP FLOORS	1085.00	1085.00
	EACH	*		
45.00	SQFT	PATRICKS BATHROOM HEX VEINING ALL GOING SAME DIRECTION, USE MORE WHITE TILES	25.00	1125.00
1.00	EACH	PATRICKS FLOOR PREP	335.00	335.00
60.00	SQFT	PATRICKS LEFT AND RIGHT WALL 8 X 12 MARBLE HORIZONTAL BRICK	20.00	1200.00

Proposal Accepted by

Date


\$42,564.00

Prices good for 30 days only. We look forward to working for you!



Total:

3567 Jess Smith Road Sophia, NC 27350 Phone: (336) 434-7433 Fax: (336) 434-1052 Email: ChampionTileCo@aol.com



Proposal Date: **08/18/2023**Proposal Number: **005977** 

Page 3 of 4

Ceramics • Marble • Pavers

## PROPOSAL

Name WOLFE HOMES

Address 220-J POMONA DRIVE

City, ST Zip GREENSBORO, NC 27407

james.wolfe@wolfehomes.com

Phone (336) 268-2018

Cell (336) 314-5146

Fax (336) 299-2949

Job Desc. 5407 EASTERN SHORES GREENSBORO / ANGELA

Qty.	Units	Description	Price	Amount
	EACH	PATRICKS BATH, POLISH VERTICAL EDGES 4 L.F.	140.00	140.00
1.00	EACH	PATRICKS BATH, BACK WALL PICTURE FRAME 55 SQFT TILE INSTALLATION	1295.00	1295.00
1.00	EACH	CAP SHELVES WITH SADDLE , INSTALLATION AND MATERIAL	170.00	170.00
1.00	EACH	PATRICKS BATH , BAND WALLS	375.00	375.00
	EACH	*		
1.00	EACH	POWDER ROOM , DIAGONAL HERRINGBONE , GREEN MARBLE 6 X 12 , 1 WALL , 65 SQ FT	3000.00	3000.00
1.00	EACH	POWDER ROOM WATERPROOFING WITH HYDROBAN , LABOR AND MATERIALS	675.00	675.00
	EACH	*		
1.00	EACH	3RD FLOOR BATH, 72 SQFT FLOOR DOUBLE HERRINGBONE MOSAIC TILE INSTALLATION .	3000.00	3000.00
1.00	EACH	3RD FLOOR BATHROOM FLOOR PREP	425.00	425.00
1.00	EACH	3RD FLOOR BATHROOM. MAIN BACK WALL LARGE FORMAT 30 X 60 TILE INSTALLATION APPROX 55 SQFT	2800.00	2800.00
1.00	EACH	3RD FLOOR BATHROOM. TWO END WALLS , LARGE FORMAT 48 X 48 TILE INSTALLATION APPROX 48 SQFT	2400.00	2400.00

Proposal Accepted by

Date

\$42,564.00

Prices good for 30 days only. We look forward to working for you!



Total:

3567 Jess Smith Road Sophia, NC 27350 Phone: (336) 434-7433

Fax: (336) 434-1052 Email: ChampionTileCo@aol.com



Proposal Date: **08/18/2023** Proposal Number: 005977

Page 4 of 4

Ceramics • Marble • Pavers

## PROPOSAL

Name WOLFE HOMES

Address 220-J POMONA DRIVE

City, ST Zip GREENSBORO, NC 27407

james.wolfe@wolfehomes.com

Phone (336) 268-2018

Cell (336) 314-5146

Fax (336) 299-2949

Job Desc. 5407 EASTERN SHORES GREENSBORO / ANGELA

Qty.	Units	Description	Price	Amount
1.00	EACH	3RD FLOOR BATHROOM. PREP WALLS. KERDI BOARD NOT INCLUDED . LABOR ONLY.	1200.00	1200.00
	EACH	*		
1.00	EACH	SETTING MATERIALS INCLUDES ALL THINSET FOR INSTALLATION OF LARGE FORMAT TILES AND STANDARD SIZE TILE, ALL FLOOR PREP LISTED ABOVE MATERIAL.	3800.00	3800.00
	EACH	THE ONLY WALL PREP WE HAVE INCLUDED IN THIS PROPOSAL IS FOR THE 3RD FLOOR BATHROOM WALLS AS INDICATED ABOVE.		1
	EACH	*		
	EACH	TILE AND GROUT ARE NOT INCLUDED. MARBLE, PLANK, GLASS, DIAGONAL, LARGE FORMAT, OR ANY SPECIAL DESIGN IS AN ADDTIONAL COST PER SQFT.		

\$42,564.00

Proposal Accepted by

Date



Total:

#### De La Torre Construction

INVOICE

INVOICE #324 DATE: 9/25/2023

TO:

Hector De La Torre De La Torre Construction 3615 Edgewood Dr Greensboro Nc, 27405 Phone: 336-451-8497 SHIP TO:

James Wolfe Wolfe Homes 200 Pomona Dr Greensboro Nc, 27407 Phone: 336-299-2969

SALESPERSON	P.O. NUMBER	REQUISITIONER	SHIPPED VIA	F.O.B. POINT	TERMS
					Due on receipt

QUANTITY	DESCRIPTION	UNIT PRICE	TOTAL
	Roof job		
	5407 eastern shores dr, Greensboro, Nc, 27455		
	Fix shingles and install flashing around the small chimney		\$180
	Made a chimney chase cover material and labor cost		\$640
		SUBTOTAL	\$820

SUBTOTAL \$820


SALES TAX

SHIPPING & HANDLING


TOTAL DUE \$820

Make all checks payable to De La Torre Construction If you have any questions concerning this invoice, contact Name, Phone, Email


THANK YOU FOR YOUR BUSINESS!

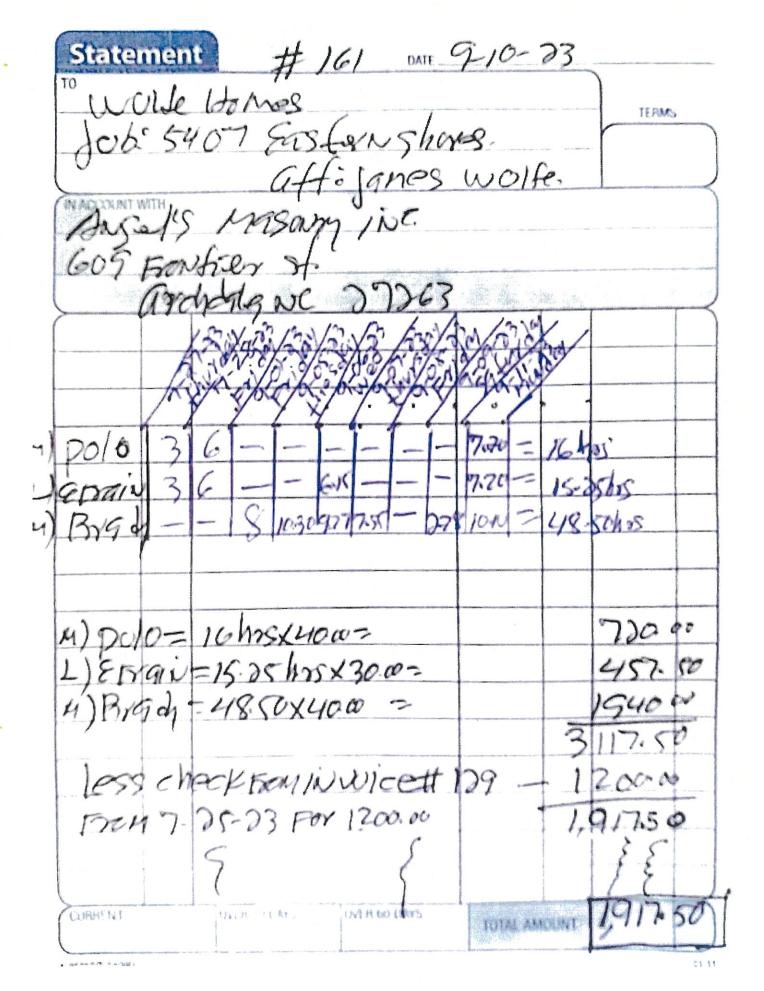

Scanned with CamScanner

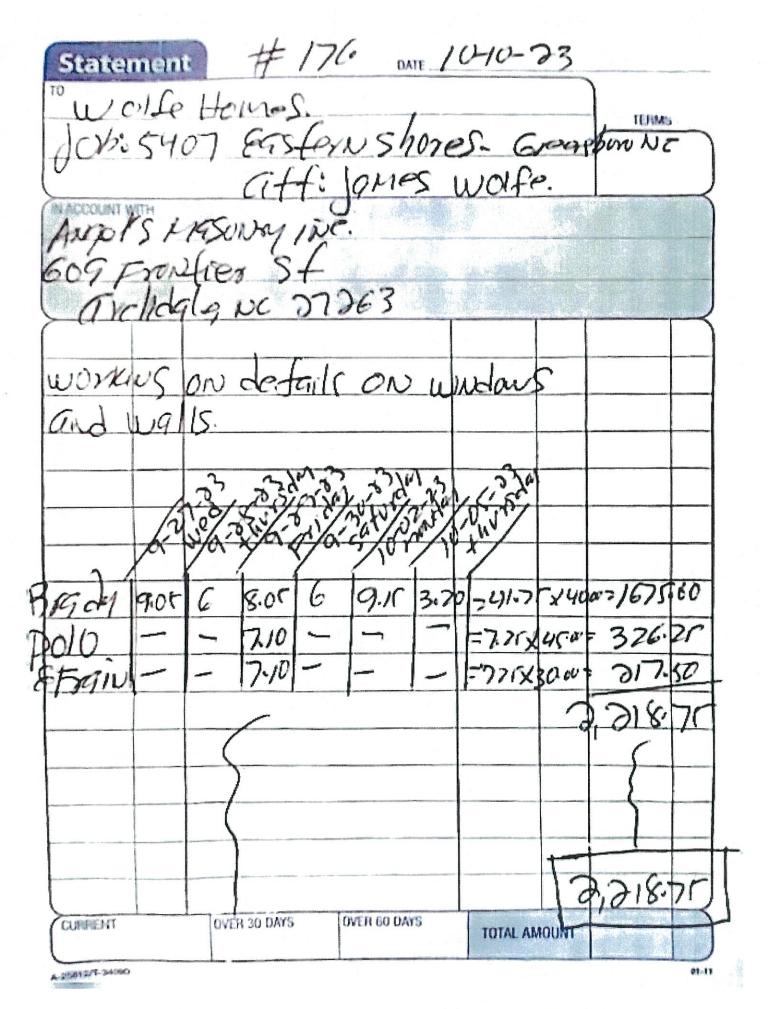

Scanned with CamScanner

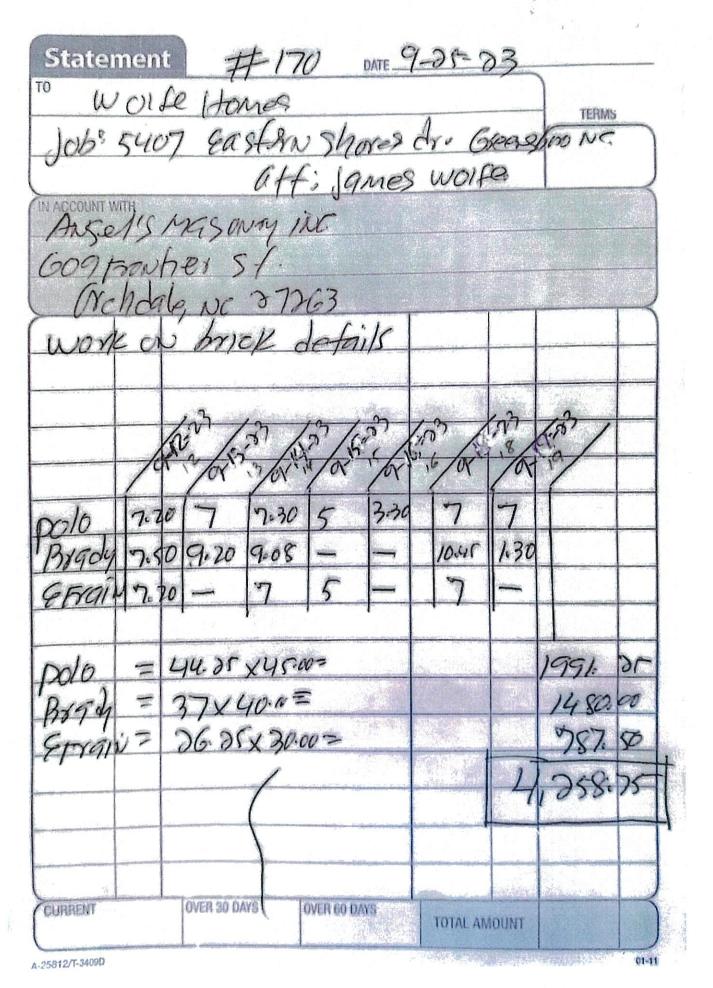

Scanned with CamScanner

#### invoice no 09/10/23/01

9/10
Job Number:
3047
TO:
Wolfe Homes
5407 Eastern Shores

Taylor Smith



Buckner Construction 5101 Summit Ave Greensboro, N.C.27405 (336) 362-6729

## **BUCKNER CONSTRUCTION**

DATE	HRS	DESCRIPTION	MEN	RATE	TOTAL
8/25	10.00 backframing		2	70.00	700.00
	4.00		1	35.00	140.00
8/28	11.50		3	105.00	1,207.50
	8.00		1	35.00	280.00
8/29	10.50	· · · · · · · · · · · · · · · · · · ·	3	105.00	1,102.50
	8.50		1	35.00	297.50
8/30	10.00		4	140.00	1,400.00
	8.00 brick demo		3	105.00	840.00
8/31	12.50		3	105.00	1,312.50
	3.50		1	35.00	122.50
9/1	11.00		3	105.00	1,155.00
	7.50		1	35.00	262.50
9/4	6.50		3	105.00	682.50
	2.50		1	35.00	87.50
				Subtotal	9,590.00

Total 9,590.00

#### invoice no 09/25/23/01

9/25 Job Number: 3047 **TO:** Wolfe Homes

TO: Wolfe Homes 5407 Eastern Shores James Wolfe Buckner Construction 5101 Summit Ave Greensboro, N.C. 27405 (336) 362-6729

## **BUCKNER CONSTRUCTION**

DATE	HRS	DESCRIPTION	MEN	RATE	TOTAL
9/11	AND DESCRIPTION OF THE PERSON	porch ceilings	3	105.00	1,102.50
3/11	8.00	por or comings	1	35.00	280.00
9/12		porch ceilings	3	105.00	997.50
3/12	8.50	por an cominge	1	35.00	297.50
9/13	9.50		3	105.00	997.50
3710	8.00		1	35.00	280.00
9/14		exterior trim	3	105.00	1,102.50
3/ 1-7	8.00	Oxtoner ann	1	35.00	280.00
9/15	8.50		4	140.00	1,190.00
9/18		backframing	4	140.00	1,680.00
9/19	11.00		3	105.00	1,155.00
0,10	10.00		1	35.00	350.00
9/20	11.00		4	140.00	1,540.00
9/21	10.50		4	140.00	1,470.00
9/22	11.00		4	140.00	1,540.00
	10.00		1	35.00	350.00
				Subtotal	14,612.50

Total 14,612.50

10/10 Job Number: 3047

TO:

Wolfe Homes 5407 Eastern Shores James Wolfe Buckner Construction 5101 Summit Ave Greensboro, N.C. 27405 (336) 362-6729

## **BUCKNER CONSTRUCTION**

DATE	HRS	DESCRIPTION	MEN	RATE	TOTAL
9/25	13.50		2	70.00	945.00
	12.50		2	70.00	875.00
	9.00		1	35.00	315.00
9/26	11.00		5	175.00	1,925.00
9/27	11.00		4	140.00	1,540.00
	6.50		1	35.00	227.50
9/28	12.00		5	175.00	2,100.00
9/29	10.50		5	175.00	1,837.50
10/2	11.50		2	70.00	805.00
	9.50		1	35.00	332.50
10/3	11.00		3	105.00	1,155.00
10/4	4.50		3	105.00	472.50
10/5	12.00		3	105.00	1,260.00
10/6	10.50		3	105.00	1,102.50
					*
				Subtotal	14,892.50

Total 14,892.50

## **Angel Painting**

1107 Alamance Church Rd 27406

Phone: 336-669-2235

INVOICE #	DATE
327	10/06/23

Job Name: 5407 Eastern Shores Drive

## **Description**

point out the garage with mud.	
Solid Mud Coat on the Bumpy area in the gym.	
Prepare the 3rd floor ,Gym ,garage to finish the last coat of mud.	

If you have any questions about this invoice, please contact
[Alondra Pahua-Vasquez #336-707 -9872 Email- Alondrapahua1889@gmail.com]

### Harrell's Waterproofing, Inc. 7103 US Hwy 158 Stokesdale, N.C. 27357

10/3/2023

#### INVOICE

Wolfe Homes A/P

Job Reference: 5407 Eastern Shores Drive in Greensboro.

Scope of work

**Deck Waterproofing** 

- -Prep the concrete deck for waterproofing
- -Apply Bituthene B2 Primer
- -Apply Bituthene System 3000 to the concrete deck
- -Apply Grace Perma Barrier through wall flashing
- -Apply PCII Board and Hydroduct Drain Mat

Total \$13,105.00

Respectfully, Greg Harrell-President CELL 336 382-0778 Your Dry Choice Since 1988!!

#### Invoice Number 0101323



Invoice Date: 10-13-23

Payment Terms: Due on Receipt

Customer:

Wolfe Homes

Invoice Details:

J5407 Eastern Shores Dr

Rail Install (2 staircases)

**Total Due:** \$1000.00

Thank you,

Meghan Robeson-Poole

Meg's Men, Inc.

203 Beckner Rd

Lexington, NC 27292

Phone 336-247-4333

#### REVCO FLOOR FINISHING INC.

4910 Mary St. GREENSBORO, NC 27409 336-855-8025

revcohardwoods@bellsouth.net

#### BILL TO

WOLFE HOMES INC. 200 - J. POMONA DR. GREENSBORO, NC 27407

## Invoice

#### SHIP TO

5407 EASTERN SHORES DR. GREENSBORO, NC 27455

INVOICE #	DATE	TOTAL DUE	DUE DATE	TERMS	ENCLOSED
5773	10/10/2023	\$1,091.00	10/25/2023	Net 15	The state of the s

DESCRIPTION	QTY	RATE	AMOUNT
5 1/4" NO.2 YELLOW PINE. 105 SQFT. @ 5.60 PER SQFT.	105	5.60	588.00
5 1/4" YELLOW PINE STAIRNOSE. 60 FT. @ 7.55 PER FT.	60	7.55	453.00
DELIVERY FEE		50.00	50.00
Thank you for your business! We accept ACH payments through this portal, which is safe and secure. Checks can be sent to 317 Pendleton Dr. Greensboro, NC 27409	BALANCE DUE	<b>\$1</b> ,	091.00

### ESPITIA CONSTRUCTION, LLC. 1008 Tuscalossa St. Greensboro NC 27406

# Invoice

Date	Invoice #
10/10/2023	4622

Bill To	
Wolfe Homes 200 J Pomona Drive Greensboro, NC 27407	
~	

		Project / Job	
		5407 Eastern Shores	
Description		Amount	
5707 Eastern Shores Dr Greensboro NC 27455			
General clean up inside and out		2,400.00	
	Т	otal \$2,400.00	

## **Daniel Griffin**

From:

Angela Toledo

Sent:

Friday, September 15, 2023 1:18 PM

To:

Invoices

Cc: Subject: James Wolfe IV Trucks and Trailers

Please charge Truck 20 to Mattern for four days on 9/5 – 9/8 @ \$100/day (\$400 total)

From:

Angela Toledo

Sent:

Wednesday, September 27, 2023 3:25 PM

To:

Invoices

Cc:

James Wolfe IV

Subject:

Trucks and Trailers

Please charge 28FT Cargo Trailer to Mattern for three days on 9/13 – 9/15 @ \$100/day (\$300 total)

From:

Angela Toledo

Sent:

Wednesday, September 27, 2023 3:25 PM

To:

Invoices

Cc:

James Wolfe IV

Subject:

Trucks and Trailers

Please charge Bobcat to Mattern for one day on 9/11 @ \$200/day (\$200 total)

From:

Angela Toledo

Sent:

Wednesday, September 27, 2023 3:28 PM

To:

Invoices

Cc:

James Wolfe IV

Subject:

Trucks and Trailers

Please charge Truck 20 to Mattern for three days on 9/11 – 9/13 @ \$100/day (\$300 total)

From:

Angela Toledo

Sent:

Wednesday, September 27, 2023 3:36 PM

To:

Invoices

Cc:

James Wolfe IV

Subject:

Trucks and Trailers

Please charge 28FT Cargo Trailer to Mattern for the entire week of 9/18 – 9/22 @ \$400/week (\$400 total)

From:

Angela Toledo

Sent:

Tuesday, October 3, 2023 2:59 PM

To:

Invoices

Cc:

James Wolfe IV

Subject:

Trucks and Trailers

Please charge 28FT Cargo Trailer to Mattern for the entire week of 9/25 – 9/29 @ \$400/week (\$400 total)

## BREWER EQUIPMENT COMPANY

SCAFFOLD & ACCESS INDUSTRY ASSOCIATION

#### **MONTHLY INVOICE**

4611 W. MARKET ST. GREENSBORO, NC 27407 336-292-6737 FAX: 336-292-2171 4594-B LONG BEACH RD. SOUTHPORT, NC 28461 910-457-0632 FAX: 910-457-0471 6600 WINDMILL WAY WILMINGTON, NC 28405 910-392-0057 FAX: 910-395-5195

# Number E40087 Date 10/13/23 Page 1

#### WWW.BREWEREQUIPMENTCO.COM

Bill To: 10252
WOLFE HOMES
200 POMONA DRIVE
SUITE J
GREENSBORO, NC 27407-1637

325.50

.00

21.97

Ship To: TEMP MATTERN #3047 5407 EASTERN SHORES DR GREENSBORO, NC 27455

Rental Pe	riod: From 09	/15/23 <b>Thru</b> 10/12/23	Pe	riods Billed:	3 Orig/	Last Ship	Date:	09/12/23
VH SIsp	Terms	Ship Via	Refe	erence No	Ordered B	y	C	Contract #
01 100	NET 30 DAYS	DELIVERED	#	#3047	JAMES WO	LFE	0	00049268
Item Code	Descripti	on		Rate/Price		Units	им	Extension
125-00	29" W	IDE X 5' HIGH LADDER E	FRAM\$	7.5000		6	EA	45.00
255-07R	TUBUL	AR CROSS BRACE - RED	\$	2.2500		6	EA	13.50
5807	7' AL:	L ALUMINUM SCAFFOLD BO	ARD\$	12.0000		3	EA	36.00
318-00	8" SC.	AFFOLD CASTER	\$	7.0000		12	EA	84.00
900-00	TOGGL	E PIN	\$	.2000		12	EA	2.40
	GATE	CODE: 7080	\$ \$ \$					
	ADD O	N TO ACT #49268	\$ \$ \$					
155-00		DE X 5' HIGH FRAME	\$	7.5000		4	EA	30.00
255-07R	TUBUL	AR CROSS BRACE - RED	\$	2.2500		4	EA	9.00
5807	7' AL:	L ALUMINUM SCAFFOLD BO	DARD\$	12.0000		4	EA	48.00
318-00	8" SC.	AFFOLD CASTER	\$	7.0000		8	EA	56.00
900-00	TOGGL	E PIN	\$	.2000		8	EA	1.60
		E	MA	ILED				
	Rentals	Sales Tax Freig	ght	Total	Paid	Dep Ap	plied	Balance

PLEASE REMIT TO: BREWER EQUIPMENT CO. 4611 W. MARKET ST. GREENSBORO, NC 27407

347.47

.00

347.47

.00

.00

## EWER EQUIPMENT COMPANY

#### MONTHLY INVOICE

4611 W. MARKET ST. GREENSBORO, NC 27407 336-292-6737 FAX: 336-292-2171

4594-B LONG BEACH RD. SOUTHPORT, NC 28461 910-457-0632 FAX: 910-457-0471

6600 WINDMILL WAY WILMINGTON, NC 28405 910-392-0057 FAX: 910-395-5195

Number	E39658
Date	09/15/23
Page	1

#### WWW.BREWEREQUIPMENTCO.COM

Bill To: 10252 **WOLFE HOMES** 200 POMONA DRIVE SUITE J GREENSBORO, NC 27407-1637 Ship To: TEMP **MATTERN #3047** 5407 EASTERN SHORES DR **GREENSBORO, NC 27455** 

K	ental Period:	From 08/18/2	3 Inru (	09/14/23	Pe	riods Billed:	2 Orig	Last Ship	Date:	09/12/23
WH	Slsp Te	erms	Ship Via		Refe	erence No	Ordered E	By	(	Contract #
01	100 NET 3	0 DAYS	DELIVERE	D	‡	¥ <b>304</b> 7	JAMES WO	LFE	(	00049268
T	Item Code	Description				Rate/Price		Units	ИМ	Extension
	125-00	29" WIDE X	5' HIGH I	ADDER FRA	М\$	7.5000		6	EA	45.00
	255-07R	TUBULAR CR	OSS BRACE	- RED	\$	2.2500		6	EA	13.5
	5807	7' ALL ALU	MINUM SCAE	FOLD BOAR	D\$	12.0000		3	EA	36.0
	318-00	8" SCAFFOI	D CASTER		\$	7.0000		12	EA	84.0
	900-00	TOGGLE PIN			\$	.2000		12	EA	2.4
		GATE CODE:	7080		\$ \$ \$					
	155-00	ADD ON TO CONTRACT # 5' WIDE X		RAME	\$ \$	7.5000		4	EA	30.0
	From 09/12/23 255-07R	To 09/15/23 TUBULAR CR	OSS BRACE	- RED	\$	2.2500		4	EA	9.0
	From 09/12/23 5807	To 09/15/23 7' ALL ALU	MINUM SCAE	FOLD BOAR	D\$	12.0000		4	EA	48.0
- 1	From 09/12/23 318-00	To 09/15/23 8" SCAFFOL	D CASTER		\$	7.0000		8	EA	56.0
- 1	From 09/12/23 900-00	To 09/15/23 TOGGLE PIN	ī		\$	.2000		8	EA	1.6
	From 09/12/23	To 09/15/23								
				EΝ	1A	ILED				
	Rentals	Sales	Tax	Freight		Total	Paid	Dep Ap	plied	Baland
-	325.50	.00	21.97	.00		347.47	.00		.00	347.4

HANNEL Change than oftens 03132023 to 1-Shorting

Report Date:

Transactions Sorted by Time and Date2

SOLID WASTE MANAGEMENT
From 08/01/2023 to 08/31/2023
Company = "48343".

Page

		\$100.98	\$61.92	\$20.40	\$70.08	\$12.00	\$17.68	\$12.00	\$41.82	\$66.64	\$19.72	\$86.36	\$104.04	591.20	\$43.18	\$49.98	\$14.62	\$86.36	\$112.80	\$21.08	\$12.00	\$20.40	\$73.10	\$36.38	\$42.16	\$77.18	\$12.00	\$33.60	\$25.92	\$38.42	\$30.60	\$27.88	\$48.28	\$26.52	\$60.52	\$12.00			
	Chg	80.00	80.00	80.00	80.00	80.00	80.00	80.00	20.00	80.00	80.00	80.00	80.00	80.00	80.00	20.00	80.00	\$0.00	80.00	80.00	20.00	20.00	80.00	80.00	80.00	20.00	80.00	80.00	80.00	80.00	80.00	80.00	20.00	20.00	80.00	80.00			
	Price	\$100.98	\$61.92	\$20.40	\$70.08	\$12.00	\$17.68	\$12.00	\$41.82	\$66.64	\$19.72	\$86.36	\$104.04	\$91.20	\$43.18	\$49.98	\$14.62	\$86.36	\$112.80	\$21.08	\$12.00	\$20.40	\$73.10	\$36.38	\$42.16	\$77.18	\$12.00	\$33.60	\$25.92	\$38 42	\$30.60	\$27.88	\$48.28	\$26.52	\$60.52	\$12.00			
	Price	34.00	48.00	34.00	48.00	34.00	34.00	34.00	34.00	34.00	34.00	34.00	34.00	49.00	34.00	34.00	34.00	34.00	48.00	34.00	34.00	34.00	34.00	34.00	34.00	34.00	34.00	48.00	48.00	34.00	34.00	34.00	34.00	34.00	34.00	34.00			
Total	Pnce	TONS	TONS	TONS	TONS	TONS	TONS	TONS	TONS	TONS	TONS	TONS	TONS	TONS	TONS	TONS	TONS	LONS	TONS	64 600 63	20.609.16																		
Fees	Name	2.97 TC		0.60 TC		0.31 TC	0.52 TC	0.25 TC		1.96 TC	0.58 TC	2.54 TC	3.06 TC		1.27 TC	1.47 TC	0.43 TC				0.20 TC	0.60 TC	2.15 TC		1.24 TC							0.82 TC		0.78 TC	1.78 TC	0.18 TC	90.03	\$0.00	
Net	Units	2940	2580	1200	2920	620	1040	200	2460	3920	1160	2080	6120	3800	2540	2940	860	2080	4700	1240	400	1200	4300	2140	2480	4540	20	1400	1080	2260	1800	1640	2840	1560	3560	360	60000	\$1,609.82	
Umt	Net	15680	9940	12160	15680	8940	10120	10240	15960	15680	9340	15680	15680	10480	15960	13060	8940	15680	9360	7640	7640	15960	15960	12980	15960	13260	8940	10120	13120	9360	8940	7680	13080	9360	15680	7780	N		
Unit	Tare	21620	12520	13360	18600	9560	11160	10740	18420	19600	10500	20760	21800	14280	18500	16000	9800	20760	14060	8880	8040	17160	20260	15120	18440	17800	0968	11520	14200	11620	10740	9320	15920	10920	19240	8140	Cardo	86280	
	Gross	CDW	MSS	CDW.	MSS	I.MII	CCV	۷.۵.۵	CDW.	CCV	IMI	LMH	IMH	NL)	CCV	CCV	CCV	CCV	DDI.	I.MH	LMH	I.MH	I.MII	CCV	CDW	CCV	CCV	MSS	DDL	TAT	CCV	CCV	CDW	CDW	LMH	LMII	OF OCCUPANT		
	Oper	CD2	1/5	CD2	T/S	CD2	CD2	CD2	CD2	CD2	CD2	CD2	CD2	1/5	CD2	CD2	CD2	CD2	SI	CD2	T/S	TIS	CD2																
	Location	_	5	_	5	_	-	_	_	-	_	_	_	5	_	_	_	_	45	_	-	_	_	_	_	_	_	45	2	_	_	_	_	_	_	51			
	Material	WH31 51	WH10 45	WH8 51	WH31 45	WH5 51	WH8 51	WH8 51	WH20 51	WH31 51	WH10 51	WH31 51	WH31 51	WH6 45	WH20 51	WH8 51	WH5 51	WH31 51	WH14 4	WH10 51	WH10 51	WH20 51	WH20 51	WH8 51	WH20 51		WH5 51	WH6 4	WH10 45	WH14 51	WH5 51	WH10 51	WH8 51	WH14 51	WH31 51	WH10 5			
Company Vehicle	GI	09:28:58 48343	14:43:23 48343	10:12:03 48343	12:23:58 48343	14:48:26 48343	12.08.41 48343	14.50.28 48343	10:08:37 48343	10.15:13 48343	13.44.29 48343	12 54,42 48343	11.05:31 48343	14 44:19 48343	08:51:26 48343	10:50:46 48343	08:17:22 48343	11:06:12 48343	12:09:33 48343	13:46:51 48343	16:49:26 48343	16:20:02 48343	10:09:38 48343	09:14:56 48343	11:31:58 48343	12:52:59 48343	13:26:40 48343	09:55:07 48343	10:08:10 48343	15:16:03 48343	10:45:36 48343	08:12:27 48343	09:26:57 48343	08:49:29 48343	12:28:55 48343	14:30:45 48343		;	43.14
Time	In ID	8/1/2023	8/1/2023	8/2/2023	8/2/2023	8/4/2023	8/7/2023	8/7/2023	8/8/2023	8/9/2023	8/9/2023	8/10/2023	8/11/2023	8/11/2023	8/14/2023	8/14/2023	8/15/2023	8/15/2023	8/16/2023	8/16/2023	8/16/2023	8/18/2023	8/19/2023	8/21/2023	8/21/2023	8/21/2023	8/22/2023	8/24/2023	8/24/2023	8/24/2023	8/28/2023	8/30/2023	8/30/2023	8/31/2023	8/31/2023	8/31/2023	,	35	
	dol,	Kumar	NG eye center			Sanders		Fitzpatrick	Mattern	3207766 Hope Academy	3207959 Hope Academy	3208357 Hope Academy	3208768 Hope Academy			Donato	Sandoval	3210256 Hope Academy		McInnis	Hall	Mattern	ALCOHOL: N		Rob Walt	Buckner	Yarborough		NG eye center	Sandoval	Stearns	Donato	NG eye center	McInnis	Rosner	Robbins			
	Ticket #	3204174	3204570 1	3204839	3204948	3206037	3206802	3206975	3207208	·3207766 +	3207959 F	3208357 1	3208768 +	3209022	3209530	3209679	3210100	3210256 F	3210849	3211087	3211088	3212232	3212422	3212778	3212915	3213032	3213613	3214475	3214490 N	3214792	3215957	3216954	3217020 1	3217475	3217707	3217841		Grand Total Tickets:	Grand Total Net Wt:

#### A SANI-CAN SERVICE, INC.

8151 Webbs Rd

Job Number:

Denver, NC 28037

**Telephone:** (336) 375-5001

Fax: (336) 375-4454

BILL TO 11830

Accounting ID:

WOLFE HOMES 200-J POMONA DR GREENSBORO, NC 27407

### Invoice

Number: 1925893

Date: 19-Sep-2023

P.O. Number:

JOB SITE 99222

5407 EASTERNSHORES DR

GREENSBORO, NC

Last Payment Date

Unpaid Balance Due:

\$166.54

28-Aug-2023

23 Late Charge:

\$0.00

From =>	To	Dur	ration	Service Type	Quantity	Price/Per	Tax?	Extension
31-Aug-2023 >	- 2	?7-Sep-2023	28	Portable Restroom Per 28-day billing cycle, in advance	1	\$71.50	<b>✓</b>	\$71.50
31-Aug-2023 >	. 2	7-Sep-2023	28	TWICE PER WEEK CLEANING Per 28-day billing cycle, in advance	1	\$65.00	<b>✓</b>	\$65.00
05-Sep-2023 >	. 2	?7-Sep-2023	23	3x PER WEEK CLEANING Per 28-day billing cycle, in advance	1	\$65.00	<b>✓</b>	\$53.39
19-Sep-2023 >	- 1	9-Sep-2023	1	.Fuel Surcharge	1	\$31.33		\$31.33

Job Site I	Balances	Taxable	Tax Rate	Tax	Description		Subtotal NonTaxed:	\$31.33
Current:	\$400.58	\$71.50	6.75	\$4.83	GUILFORD COUNTY		Subtotal Taxable:	\$189.89
30-Day:	\$0.00						Subtotal Tax:	\$12.82
60-Day:	\$0.00	\$118.39	6.75	\$7.99	GUILFORD COUNTY		Current Invoice Total:	\$234.04
90-Day+:	\$0.00							Ψ201.01
Total:	\$400.58	Terms: No	et 10	+/- Chro	g or Pymt:	\$0.00	Please Pay:	\$400.58

Attached are the invoices for your account. Invoice questions can be directed to AR@Asanican.com. Please note our mailing address has change

From:

WOLFE HOMES 200-J POMONA DR GREENSBORO, NC 27407 Please detach and return the bottom portion with payment.

Invoice No. Date

1925893 19-Sep-2023

Unpaid Balance Due

\$234.04 \$166.54

Current Amount

Please Pay:

\$400.58

To:

To pay using your credit card, please fill in this information:

A SANI-CAN SERVICE, INC.

8151 Webbs Rd

Denver, NC 28037

Credit Card Number

Date Expires

Sec Cd

Signature

Check to enroll in auto-pay

Amount to Pay or leave blank to pay in full

## ASB Portable Toilets, Inc.

2544 Alamance Church Rd.
Greensboro, NC 27406
accounting@abportabletoilets.com

336-697-8111 Phone # 336-697-2909 Fax #

## INVOICE

Date 10/8/2023
Invoice # CRO99712

Terms Net 10

#### Bill To:

WOLFE Homes 200 Pomona Dr Greensboro, NC 27407

#### Ship To:

WOLFE Homes - 5407 Eastern Shores 5407 Eastern Shores Drive Greensboro, North P.O. No.

Ship Date 10/8/2023

Project WOLFE Homes - 5407 E...

Qty	Description	Rate	Amount
1	Delivery of Const Port A Jon (#NN172298 - 1 CONSTRUCTION PJ) #264925 on 09/15/2023	0.00	0.00T
1	Delivery of Const Port A Jon (#MM128884 - 1 CONSTRUCTION PJ) #267344 on 09/27/2023	0.00	0.00T
23	Proration of Const Port A Jon (09/15/2023 to 10/08/2023)	5.4882	126.23T
1	Service of Const Port A Jon	153.67	153.67T
11	Proration of Const Port A Jon (09/27/2023 to 10/08/2023)	5.4882	60.37T
1	Service of Const Port A Jon	153.67	153.67T
2	Fuel Surcharge	15.00	30.00T

PLEASE DETACH AND RETURN BOTTOM PORTION WITH PAYMENT

Total

\$559.31

#### From:

WOLFE Homes 200 Pomona Dr Greensboro, NC 27407

Please make checks payable to:

A&B Portable Toilets, Inc.

2544 Alamance Church Rd. Greensboro, NC 27406

#### REMITTANCE

 Date
 10/8/2023

 Invoice #
 CRO99712

 Sales Tax (6.75%)
 \$35.37

 Payments/Credits
 \$0.00

 Balance Due
 \$559.31

There will be a \$30 charge for all returned checks along with a 10% interest charge will be assessed on all unpaid balances after 90 days.



BILL TO

Wolfe Homes

200 Pomona Dr. Suite J

Greensboro, NC 27407

**INVOICE # 143126** 

**DATE** 09/18/2023

**DUE DATE 10/18/2023** 

TERMS Net 30

#### DRIVER

SC

DATE	DESCRIPTION	QTY	RATE	AMOUNT
09/15/2023	Location- 5407 Eastern Shores Dr.	1	0.00	0.00
09/15/2023	Container Type- 30 Yard Open Top	1 4	0.00	0.00
09/15/2023	Haul Charge	1	120.00	120.00
09/15/2023	Landfill Charge	1	184.32	184.32
09/15/2023	Fuel Surcharge	1	30.00	30.00

Due to rising fuel costs all hauls are subject to a \$30.00 fuel surcharge.

**BALANCE DUE** 

\$334.32

Remit to: Carolina Disposal Service, Inc.

816 Shady Hanes Rd. Lexington, NC 27295 (336)731-7777



BILL TO

Wolfe Homes

200 Pomona Dr. Suite J Greensboro, NC 27407 **INVOICE # 143851** 

**DATE** 10/04/2023

**DUE DATE** 11/03/2023

TERMS Net 30

#### DRIVER

CC

DATE	DESCRIPTION	QTY	RATE	AMOUNT
09/25/2023	Location- 5407 Eastern Shores Dr.	1	0.00	0.00
09/25/2023	Container Type- 30 Yard Open Top	1	0.00	0.00
09/25/2023	Haul Charge	1	120.00	120.00
09/25/2023	Landfill Charge	1	187.68	187.68
09/25/2023	Fuel Surcharge	1	30.00	30.00

Due to rising fuel costs all hauls are subject to a \$30.00 fuel surcharge.

**BALANCE DUE** 

\$337.68

Remit to: Carolina Disposal Service, Inc. 816 Shady Hanes Rd. Lexington, NC 27295 (336)731-7777



BILL TO

Wolfe Homes

200 Pomona Dr. Suite J

Greensboro, NC 27407

**INVOICE # 142843** 

**DATE** 09/11/2023

**DUE DATE 10/11/2023** 

TERMS Net 30

#### DRIVER

SC

DATE	DESCRIPTION	QTY	RATE	AMOUNT
09/07/2023	Location- 5407 Eastern Shores Dr.	1	0.00	0.00
09/07/2023	Container Type- 30 Yard Open Top	1	0.00	0.00
09/07/2023	Haul Charge	1	120.00	120.00
09/07/2023	Landfill Charge	1	400.80	400.80
09/07/2023	Fuel Surcharge	1	30.00	30.00

Due to rising fuel costs all hauls are subject to a \$30.00 fuel surcharge.

**BALANCE DUE** 

\$550.80

Remit to: Carolina Disposal Service, Inc. 816 Shady Hanes Rd.

Lexington, NC 27295

(336)731-7777



**BILL TO** 

Wolfe Homes

200 Pomona Dr. Suite J Greensboro, NC 27407 **DUE DATE 11/12/2023** 

TERMS Net 30

**DATE** 10/13/2023

**INVOICE # 144560** 

DRIVER

SC

DATE	DESCRIPTION	QTY	RATE	AMOUNT	
10/12/2023	Location- 5407 Eastern Shores Dr.	1	0.00	0.00	
10/12/2023	Container Type- 30 Yard Open Top	1	0.00	0.00	
10/12/2023	Haul Charge	1	120.00	120.00	
10/12/2023	Landfill Charge	1	169.92	169.92	
10/12/2023	Fuel Surcharge	1	30.00	30.00	

Due to rising fuel costs all hauls are subject to a \$30.00 fuel surcharge.

**BALANCE DUE** 

\$319.92

Remit to: Carolina Disposal Service, Inc. 816 Shady Hanes Rd. Lexington, NC 27295

(336)731-7777

Remit To:

RENTAL WORKS 801 E WENDOVER AVE GREENSBORO, NC 27405

rentalworksgreensboro.com



#### Invoice

Continued	Invoice#
Fri 9/29/2023	48898

Customer #: 1024

WOLFE HOMES 200 J POMONA DR.

GREENSBORO, NC 27407

Job Descr: 19' SCISSOR

Job No: \*

Date Out Thu 8/31/2023

Terms	Aging Date
On Account	Fri 9/29/2023

ordered	By: TAYLOR 336-908-9976		ndandaritzykolokolokolokolokolokolokolokolokolokol		
Qty	Items Rented	Ser#	Status	Rental Period	Price
. 1	SCISSOR LIFT 19 FT ELEC		Billed To	Thu 8/31/2023 to Thu 9/28/2023	\$650.00
	Called Off #24597 on 7/25/2023 for 7/25/2023: Called Off	#24977 on 8/14/2023 for 8/14/2023			
Qty	Items Sold		Status	Each	Price
1	DELIVERY, PER MILE		Sold	\$125.00	\$125.00
1	PICKUP, PER MILE		Sold	\$125.00	\$125.00

Delivery Thu 8/31/2023 11:30AM

TAYLOR 336-908-9976

Pickup Thu 9/28/2023 4:30PM

TAYLOR 336-908-9976

5407 EASTERN SHORES DR GREENSBORO, NC 27455 5407 EASTERN SHORES DR GREENSBORO, NC 27455

ALREADY HAVE A SCISSOR LIFT THERE JAMES WOLF WANTED A SECOND

#### Current On Account

Please pay from this invoice. Any pick up date listed is an estimate based on the rental period. Customer must call during the rental period to schedule the pick up and obtain a Called-Off Rent number before the rental will end and a pick up will occur.

Rental and Sales:	The state of the s						Gree	ensboro Tax:
\$900.00	A PART AND							\$60.75
Total Amount:	\$960.75	<del></del>	ngga mat salawaya bodawan inga salawan ga doga mineran ga mar an anyas an awa awa awa salawa sa salawa sa sa	Total Paid	\$0.00	Total	Due:	\$960.75

336-275-9788 Phone

rentalworksgreensboro.com

RENTAL WORKS 801 E WENDOVER AVE GREENSBORO, NC 27405

rentalworksgreensboro.com



#### Invoice

Continued	Invoice#
Thu 10/ 5/2023	49113

Customer #: 1024

WOLFE HOMES 200 J POMONA DR.

GREENSBORO, NC 27407

Job Descr: 5K FORKLIFT

PO #: 3047 Job No: 3047

Date Out Wed 9/ 6/2023

Terms	Aging Date
On Account	Thu 10/ 5/2023

rdered l	By: JAMES WOLFE	336 317-9960			CANDENNO E ELECTRONALE ELECTRONALE ELECTRONALE EL PRESENTANTO ANTICONO DE CANDO DE LA CONTRACTORIO DE LA CON	THE PROPERTY OF THE PROPERTY O
Qty		Items Rented	Ser#	Status	Rental Period	Price
1		FORKLIFT 5000LB INDUSTRIAL	A5BB30219	Billed To	Wed 9/ 6/2023 to Wed 10/ 4/2023	\$1,495.00
	Meter Out: 456.8					
Qty		Items Sold		Status	Each	Price
5		DELIVERY, PER MILE	A CONTRACTOR OF THE PROPERTY O	Sold	\$25.00	\$125.00
5		PICKUP, PER MILE		Sold	\$25.00	\$125.00

Delivery Wed 9/ 6/2023 2:00PM

STEVEN 256-565-2019

5407 EASTERN SHORES DR GREENSBORO, NC 27409 GATE CODE 7080 Pickup Wed 10/ 4/2023 2:00PM

STEVEN 256-565-2019

5407 EASTERN SHORES DR GREENSBORO, NC 27409

#### Current On Account

Please pay from this invoice. Any pick up date listed is an estimate based on the rental period. Customer must call during the rental period to schedule the pick up and obtain a Called-Off Rent number before the rental will end and a pick up will occur.

		CONTRACTOR OF A THE SAME OF A THE SAME OF A SA		The second secon	The second secon
Rental and Sales:					Greensboro Tax:
\$1,745.00	DOWNSON OF THE PARTY OF THE PAR				\$117.79
Total Amount:	\$1,862.79	Total Paid	\$0.00	Total Due	\$1,862.79

336-275-9788 Phone

rentalworksgreensboro.com

RENTAL WORKS 801 E WENDOVER AVE GREENSBORO, NC 27405

rentalworksgreensboro.com



#### Invoice

Continued	Invoice#
Fri 9/22/2023	48601

Customer #: 1024

WOLFE HOMES 200 J POMONA DR.

GREENSBORO, NC 27407

Job Descr: BOOM LIFT 80FT

Job No: -

Date Out Thu 8/24/2023

Terms	Aging Date
 On Account	Fri 9/22/2023

Qty		Items Rented	Ser#	Status	Rental Period	Pric
1	ACCURATION AND THE PROCESS OF THE PR	BOOM 80' ARTICULATING 4WD W/JIB	0300172101	Billed To	Thu 8/24/2023 to Thu 9/21/2023	\$4,700.00
	Meter Out: 3466.0	TO SANDERS OF THE PROPERTY OF	TO CHARLES AND CRAFF CRAFF CONTROL OF CONTRO	nder geronen zu etnem eine Konstell bei der Vereinne kreit stade ein fluster ein fluster ein der		
STATE OF THE PERSON NAMED IN COLUMN 1 IS NOT THE OWNER.		and the control of th		Ctatus	Each	Price
Qty		Items Sold		Status	Lacii	1110
Qty 1		Items Sold  DELIVERY, PER MILE		Sold	\$125.00	\$125.00

Delivery Thu 8/24/2023 8:00AM

TAYLOR 336-908-9976

5407 EASTERN SHORES DR GREENSBORO, NC 27455 Pickup Thu 9/21/2023 8:00AM

TAYLOR 336-908-9976

5407 EASTERN SHORES DR GREENSBORO, NC 27455

#### Current On Account

Please pay from this invoice. Any pick up date listed is an estimate based on the rental period. Customer must call during the rental period to schedule the pick up and obtain a Called-Off Rent number before the rental will end and a pick up

will occur.

Rental and Sales:						Greensboro Tax:
\$4,950.00						\$334.12
Total Amount: \$5,	,284.12	austrus area comunity establistic confirment in confirment and are some size destablishment of the area.	Total Paid	\$0.00	Total	Due: \$5,284.12

336-275-9788 Phone

rentalworksgreensboro.com
